




CIVIL ENGINEERING

# Issued Programme November 2024

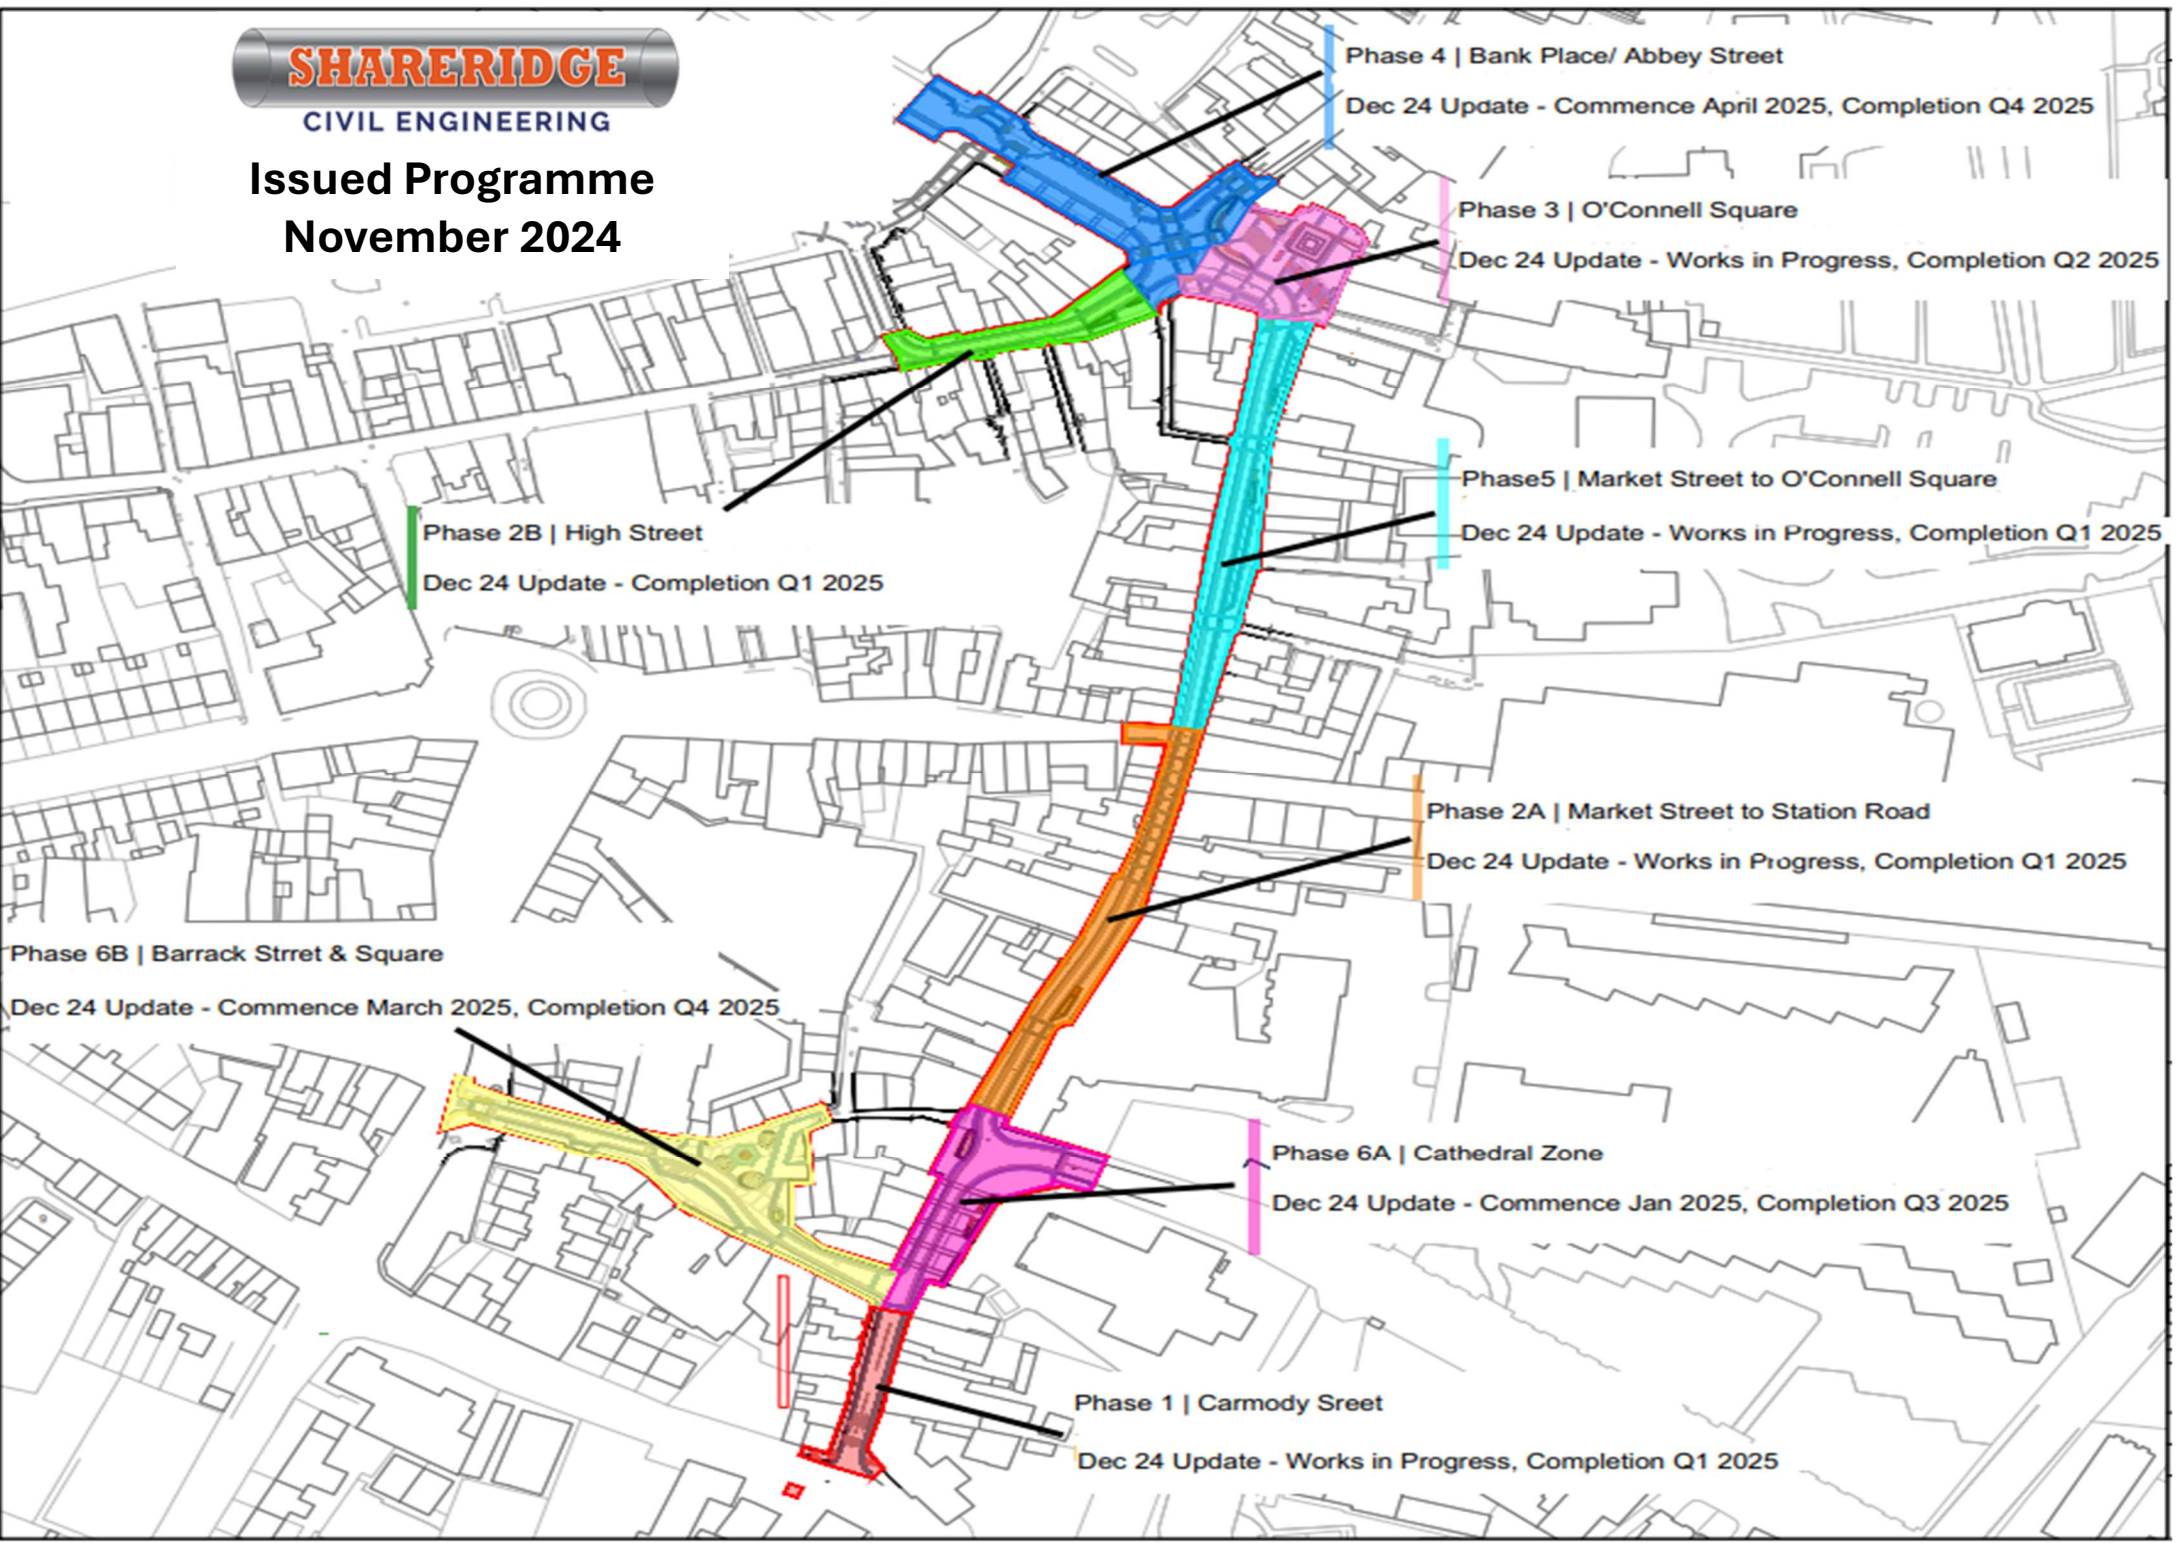

Phase 4 | Bank Place/ Abbey Street

Dec 24 Update - Commence April 2025, Completion Q4 2025

Phase 3 | O'Connell Square

Dec 24 Update - Works in Progress, Completion Q2 2025

Phase 5 | Market Street to O'Connell Square

Dec 24 Update - Works in Progress, Completion Q1 2025

Phase 2B | High Street

Dec 24 Update - Completion Q1 2025

Phase 2A | Market Street to Station Road

Dec 24 Update - Works in Progress, Completion Q1 2025

Phase 6B | Barrack Street & Square

Dec 24 Update - Commence March 2025, Completion Q4 2025

Phase 6A | Cathedral Zone

Dec 24 Update - Commence Jan 2025, Completion Q3 2025

Phase 1 | Carmody Street

Dec 24 Update - Works in Progress, Completion Q1 2025
